





























































































ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
1			Third-Eye Project	102 days	Fri 12/5/14	Mon 4/27/15	
2			Meeting with Customer	42 days	Fri 12/5/14	Mon 2/2/15	
3			Acquire & Define Problem	3 days	Fri 12/5/14	Tue 12/9/14	
4			Gather Requirements	3 days	Wed 12/10/14	Fri 12/12/14	3
5			Brief Q&A to Refine Problem Details	1 day	Wed 12/10/14	Wed 12/10/14	3
6			Present Problem (First Meeting)	3 days	Thu 12/11/14	Mon 12/15/14	
7			Review Problem Details	1 day	Thu 12/11/14	Thu 12/11/14	5
8			Analyze Requirements	1 day	Mon 12/15/14	Mon 12/15/14	4,7
9			Determine Project Feasibility	6 days	Wed 12/10/14	Wed 12/17/14	
10			Research Existing Solutions	2 days	Wed 12/10/14	Thu 12/11/14	3
11			Produce Research Documentation	1 day	Fri 12/12/14	Fri 12/12/14	10
12			Discussions (2nd Meeting)	2 days	Mon 12/15/14	Tue 12/16/14	
13			Discuss Existing Solutions	1 day	Mon 12/15/14	Mon 12/15/14	11
14			Discuss Possible Solutions	1 day	Tue 12/16/14	Tue 12/16/14	13
15			Construct Feasible Solution	3 days	Mon 12/15/14	Wed 12/17/14	
16			Refine Technology Research	1 day	Wed 12/17/14	Wed 12/17/14	14
17			Refine Requirements	2 days	Mon 12/15/14	Tue 12/16/14	4
18			Project Preparations	34 days	Wed 12/17/14	Mon 2/2/15	
19			Prepare Preliminary Design Plans	11 days	Wed 12/17/14	Wed 12/31/14	
20			Construct Preliminary Architecture	10 days	Wed 12/17/14	Tue 12/30/14	
21			Produce Top-Level Components	5 days	Wed 12/17/14	Tue 12/23/14	17
22			Construct Basic Design Modules	5 days	Wed 12/24/14	Tue 12/30/14	21
23			Organize Requirements and Specifications	1 day	Wed 12/31/14	Wed 12/31/14	






















Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors
24		Prepare Requirements Checklist	1 day	Wed 12/31/14	Wed 12/31/14	22
25		Incorporate Spec into Design Modules	1 day	Wed 12/31/14	Wed 12/31/14	22
26		Finalize Preliminary Design Plans	21 days	Thu 1/1/15	Thu 1/29/15	
27		Communicate with Customer	1 day	Thu 1/1/15	Thu 1/1/15	25
28		Present Preliminary Plans	1 day	Fri 1/2/15	Fri 1/2/15	27
29		Confirm/Clarify Customer Expectations	6 days	Mon 1/5/15	Mon 1/12/15	28
30		Acquire Preliminary Design Approval	13 days	Tue 1/13/15	Thu 1/29/15	29
31		Team Meeting	2 days	Fri 1/30/15	Mon 2/2/15	
32		Organize Design Teams	1 day	Fri 1/30/15	Fri 1/30/15	30
33		Assign Design Tasks	1 day	Mon 2/2/15	Mon 2/2/15	32
34		Design and Planning	33 days	Fri 1/30/15	Tue 3/17/15	
35		Designing	33 days	Fri 1/30/15	Tue 3/17/15	
36		Top-Level Designs	33 days	Fri 1/30/15	Tue 3/17/15	
37		Specify Architecture Details	7 days	Fri 1/30/15	Mon 2/9/15	
38		Construct Block Diagram	4 days	Fri 1/30/15	Wed 2/4/15	30
39		Add Data Flow Information	3 days	Thu 2/5/15	Mon 2/9/15	38
40		Define Major Modules:	26 days	Tue 2/10/15	Tue 3/17/15	
41		Control Module	19 days	Tue 2/10/15	Fri 3/6/15	
42		User Interface	17 days	Tue 2/10/15	Wed 3/4/15	39
43		Audio Feedback	16 days	Tue 2/10/15	Tue 3/3/15	39
44		Tactile Feedback	19 days	Tue 2/10/15	Fri 3/6/15	39






















Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	


ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors
45		Location	16 days	Tue 2/10/15	Tue 3/3/15	39
46		Third-Eye Server	16 days	Tue 2/10/15	Tue 3/3/15	
47		Database	16 days	Tue 2/10/15	Tue 3/3/15	39
48		Map Querying	15 days	Tue 2/10/15	Mon 3/2/15	39
49		Speech Recognition Module	16 days	Tue 2/10/15	Tue 3/3/15	39
50		Map Generator	26 days	Tue 2/10/15	Tue 3/17/15	
51		User Interface	26 days	Tue 2/10/15	Tue 3/17/15	39
52		Low-Level Designs	8 days	Wed 3/4/15	Fri 3/13/15	
53		Server Software Design	8 days	Wed 3/4/15	Fri 3/13/15	
54		Specify Sub-Module Design	8 days	Wed 3/4/15	Fri 3/13/15	
55		Database Design	8 days	Wed 3/4/15	Fri 3/13/15	47
56		Production	60 days	Fri 1/30/15	Thu 4/23/15	
57		Production Preparations	45 days	Fri 1/30/15	Thu 4/2/15	
58		Purchase Test Equipment	12 days	Wed 3/18/15	Thu 4/2/15	40
59		Team Meeting	1 day	Fri 1/30/15	Fri 1/30/15	
60		Organize Development Team	1 day	Fri 1/30/15	Fri 1/30/15	30
61		Assign Coding Tasks	1 day	Fri 1/30/15	Fri 1/30/15	30
62		Software Development	59 days	Mon 2/2/15	Thu 4/23/15	
63		Control Module	26 days	Mon 2/2/15	Mon 3/9/15	
64		User Interface	26 days	Mon 2/2/15	Mon 3/9/15	61
65		Audio Feedback	23 days	Mon 2/2/15	Wed 3/4/15	61
66		Tactile Feedback	25 days	Mon 2/2/15	Fri 3/6/15	61
67		Location	24 days	Mon 2/2/15	Thu 3/5/15	61
68		Third-Eye Server	25 days	Mon 2/2/15	Fri 3/6/15	

Project: Third-Eye Developmen Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID	 Task Mode	Task Name	Duration	Start	Finish	Predecessors
69		Database	25 days	Mon 2/2/15	Fri 3/6/15	61
70		Map Querying	23 days	Mon 2/2/15	Wed 3/4/15	61
71		Speech Recognition Module	19 days	Mon 2/2/15	Thu 2/26/15	61
72		Map Generator	59 days	Mon 2/2/15	Thu 4/23/15	
73		User Interface	29 days	Mon 2/2/15	Thu 3/12/15	61
74		Pre-Deployment Testing	12 days	Fri 3/13/15	Mon 3/30/15	73
75		Integrate Core Components	18 days	Tue 3/31/15	Thu 4/23/15	74
76		Test Integrated System	1 day	Tue 3/31/15	Tue 3/31/15	74
77		Confirm Success of Test	1 day	Wed 4/1/15	Wed 4/1/15	76
78		Purchases	12 days	Thu 4/2/15	Fri 4/17/15	
79		Hardware	12 days	Thu 4/2/15	Fri 4/17/15	77
80		Software	1 day	Thu 4/2/15	Thu 4/2/15	77
81		Documentation	13 days	Thu 4/2/15	Mon 4/20/15	
82		Manual	13 days	Thu 4/2/15	Mon 4/20/15	77
83		Deployment	18 days	Thu 4/2/15	Mon 4/27/15	
84		Install Servers	5 days	Thu 4/2/15	Wed 4/8/15	77
85		Setup Application Distribution	1 day	Thu 4/2/15	Thu 4/2/15	77
86		Testing	12 days	Thu 4/9/15	Fri 4/24/15	84
87		Customer Training	1 day	Thu 4/2/15	Thu 4/2/15	77
88		Full System Demonstration	1 day	Mon 4/27/15	Mon 4/27/15	86



Project: Third-Eye Developmen Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

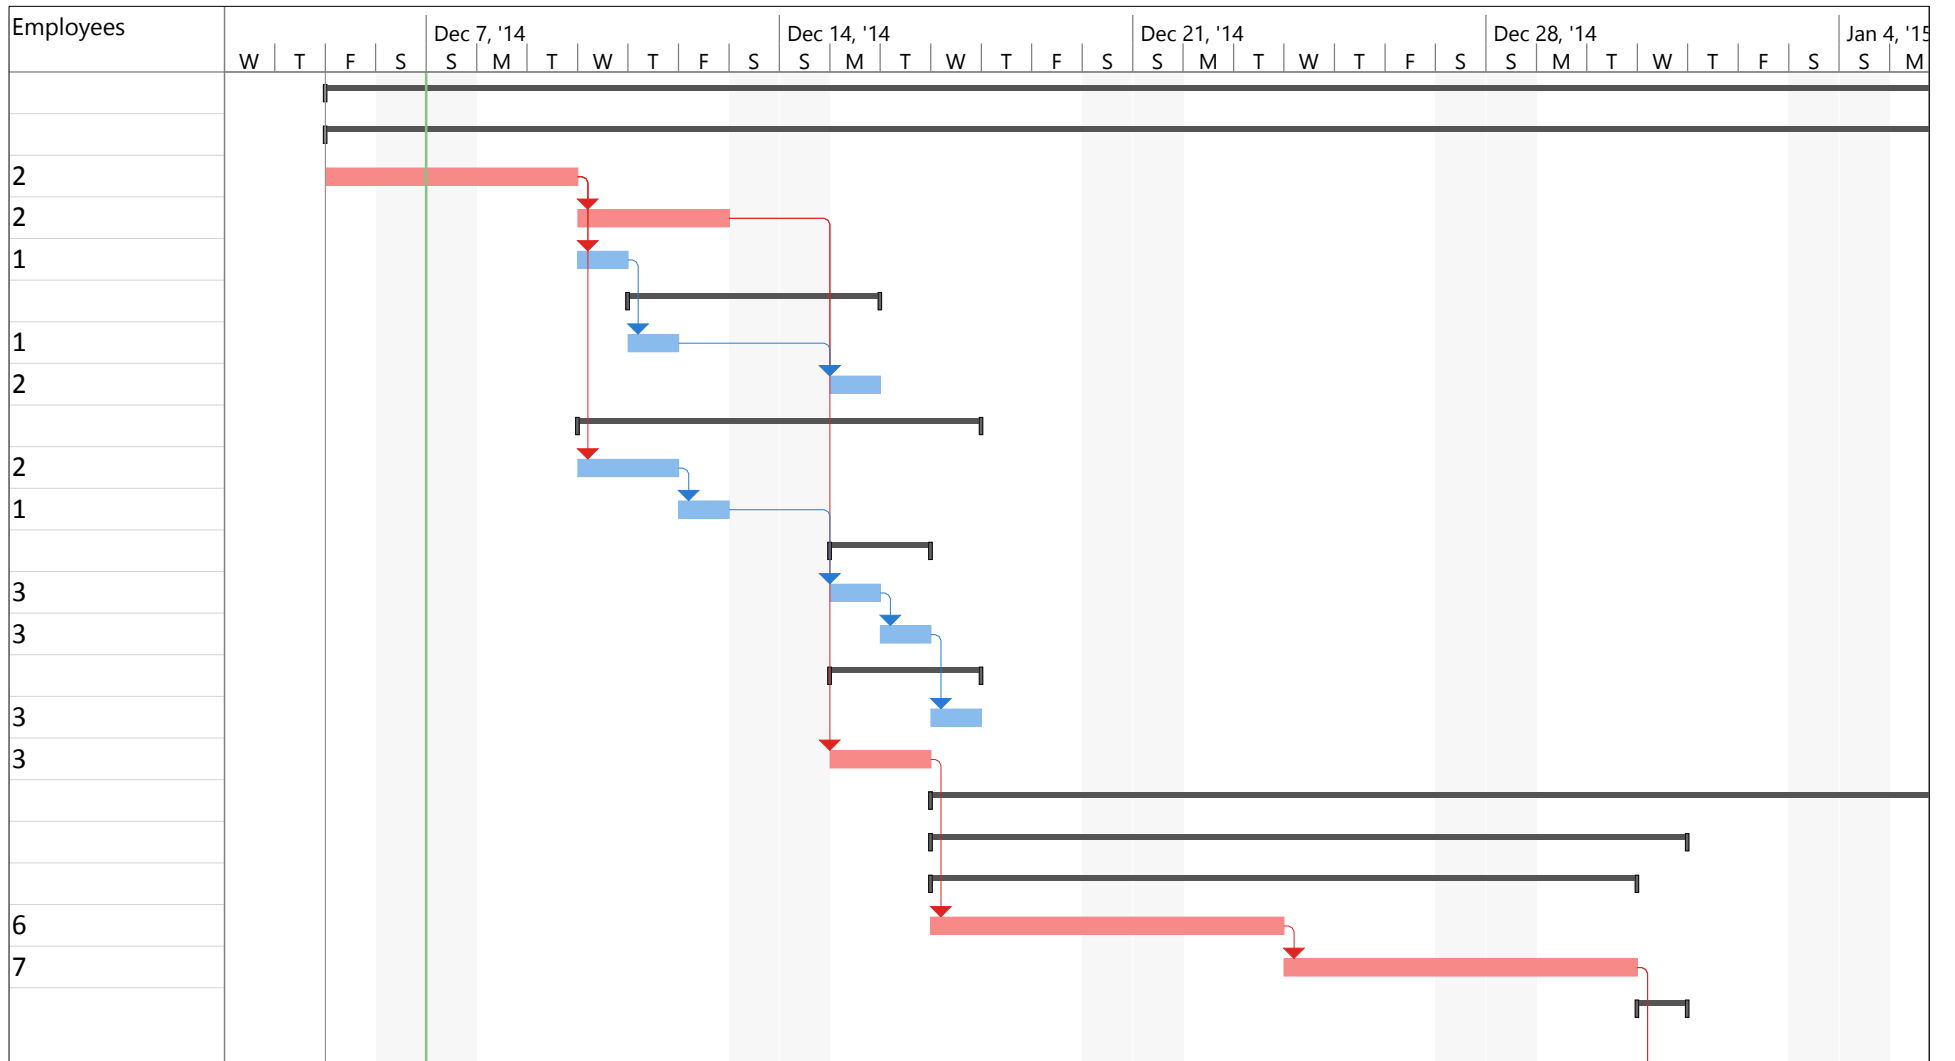


Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	


Employees	Dec 7, '14				Dec 14, '14				Dec 21, '14				Dec 28, '14				Jan 4, '15										
	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
4																											
5																											
5																											
5																											
4																											
5																											
5																											
2																											
5																											
4																											
5																											
5																											

Project: Third-Eye Development
Date: Sun 12/7/14


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

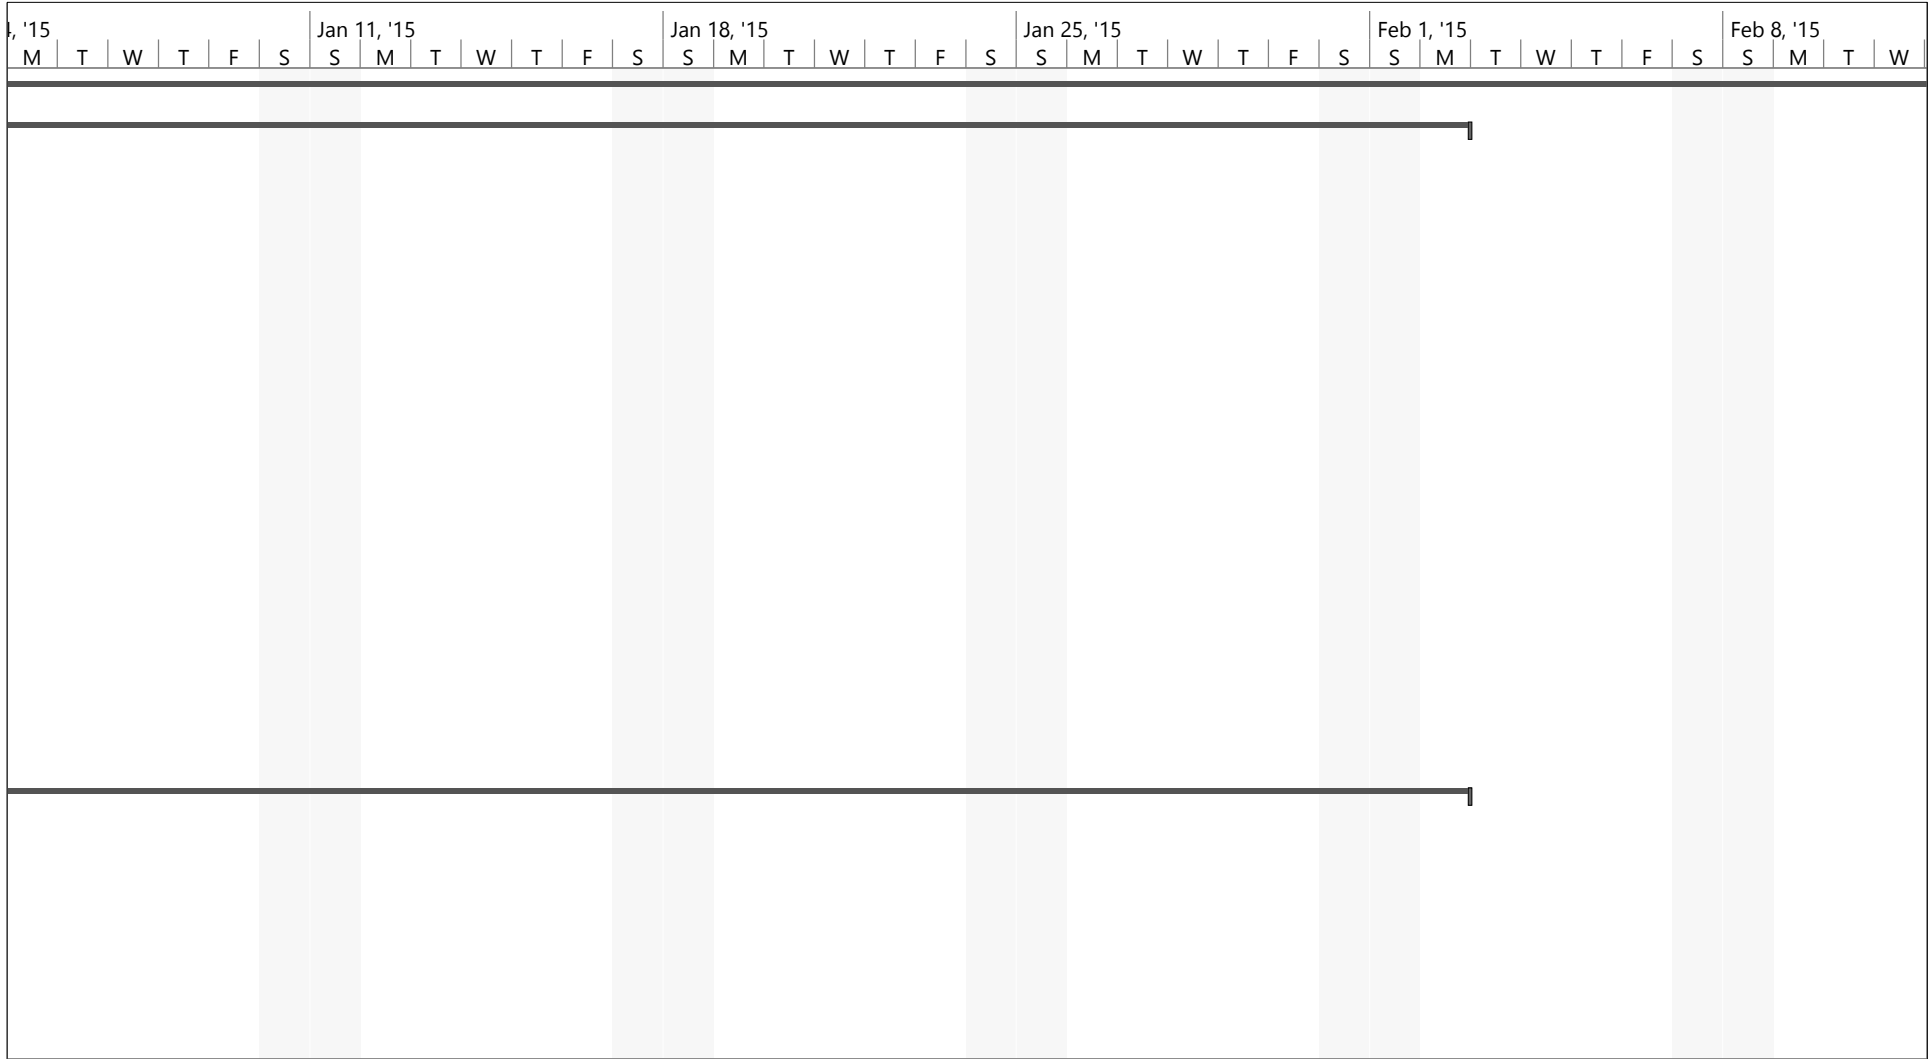

Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

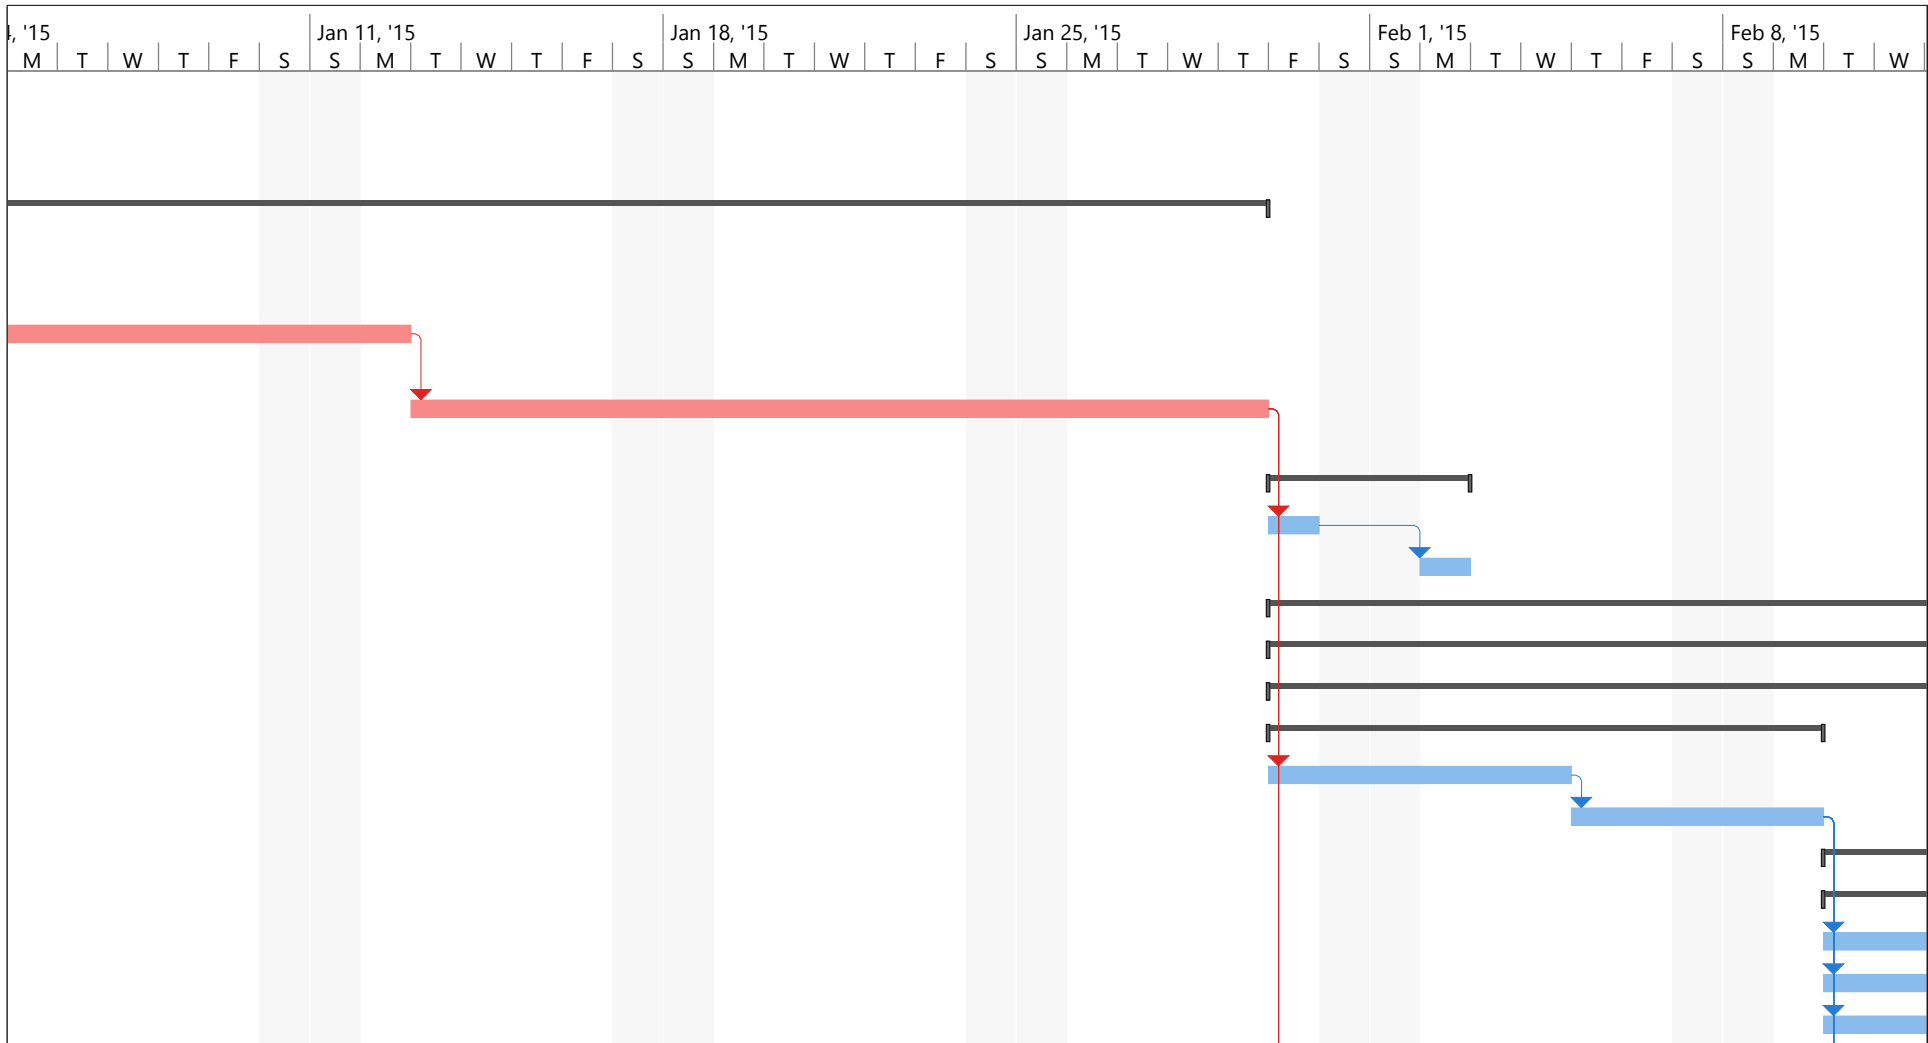


Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

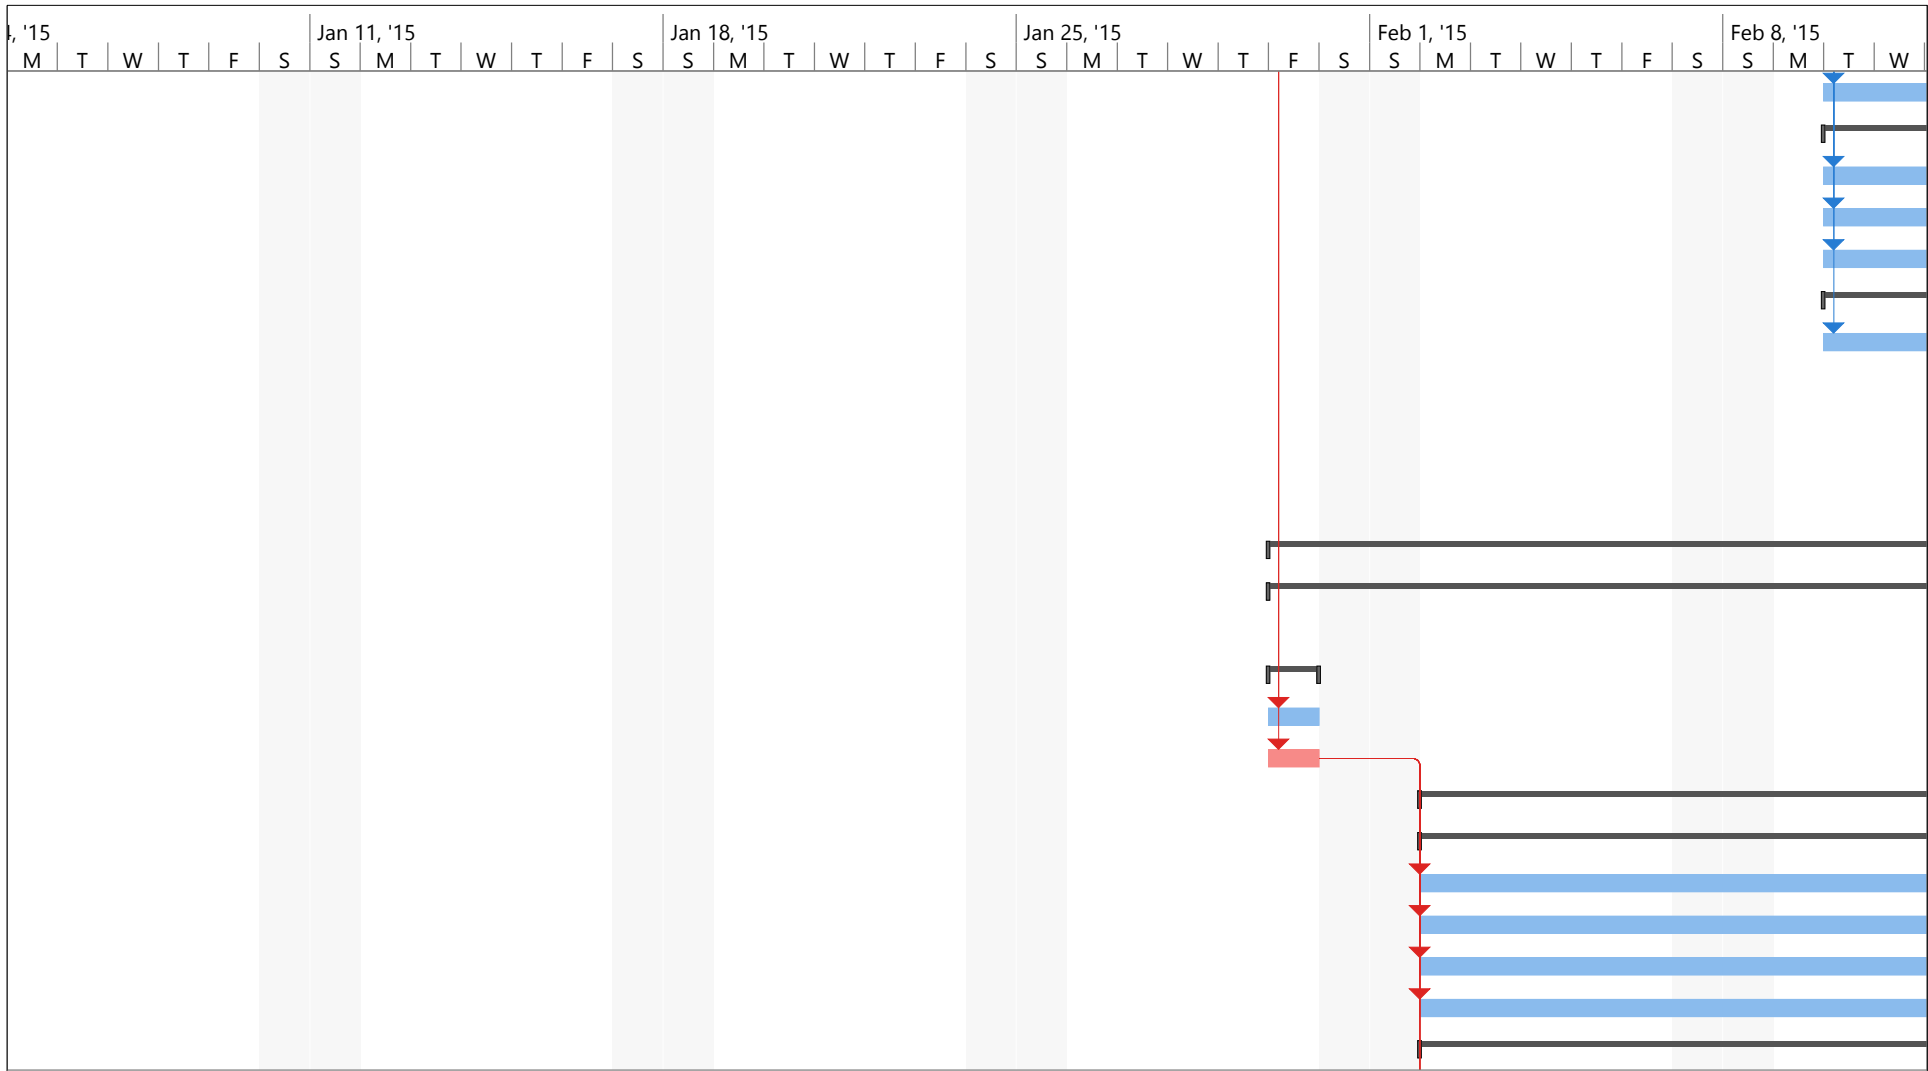


Project: Third-Eye Development
 Date: Sun 12/7/14


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

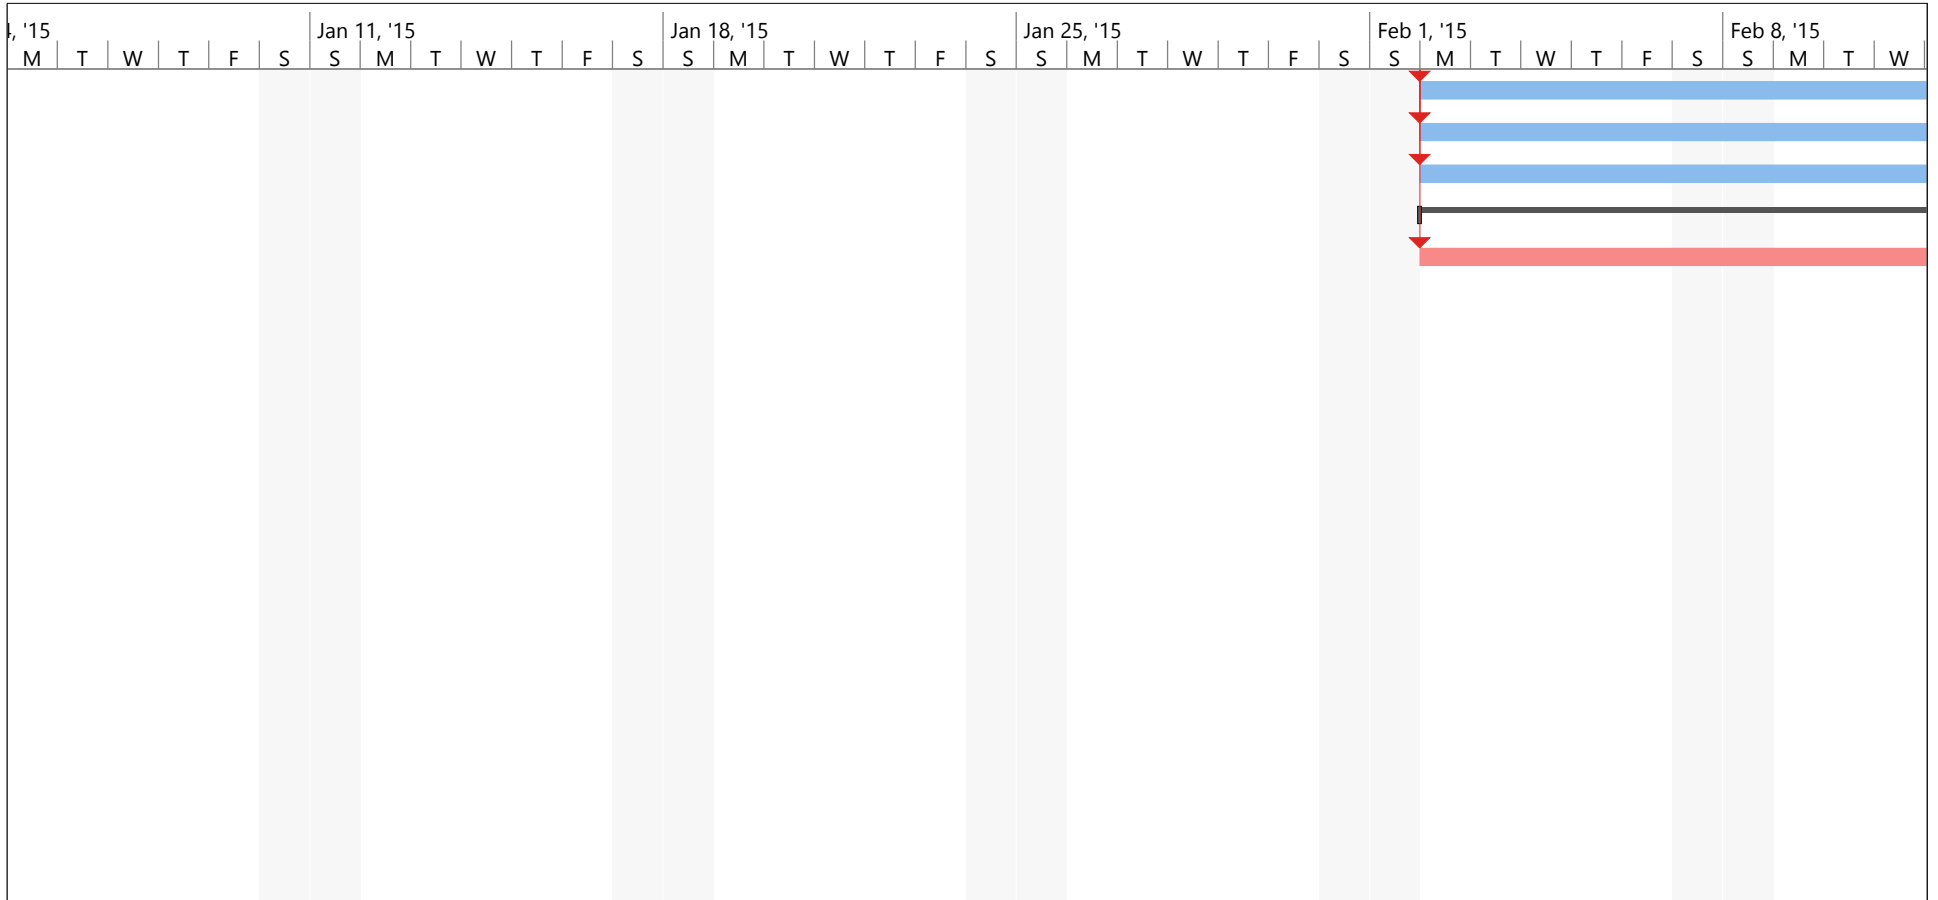


Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

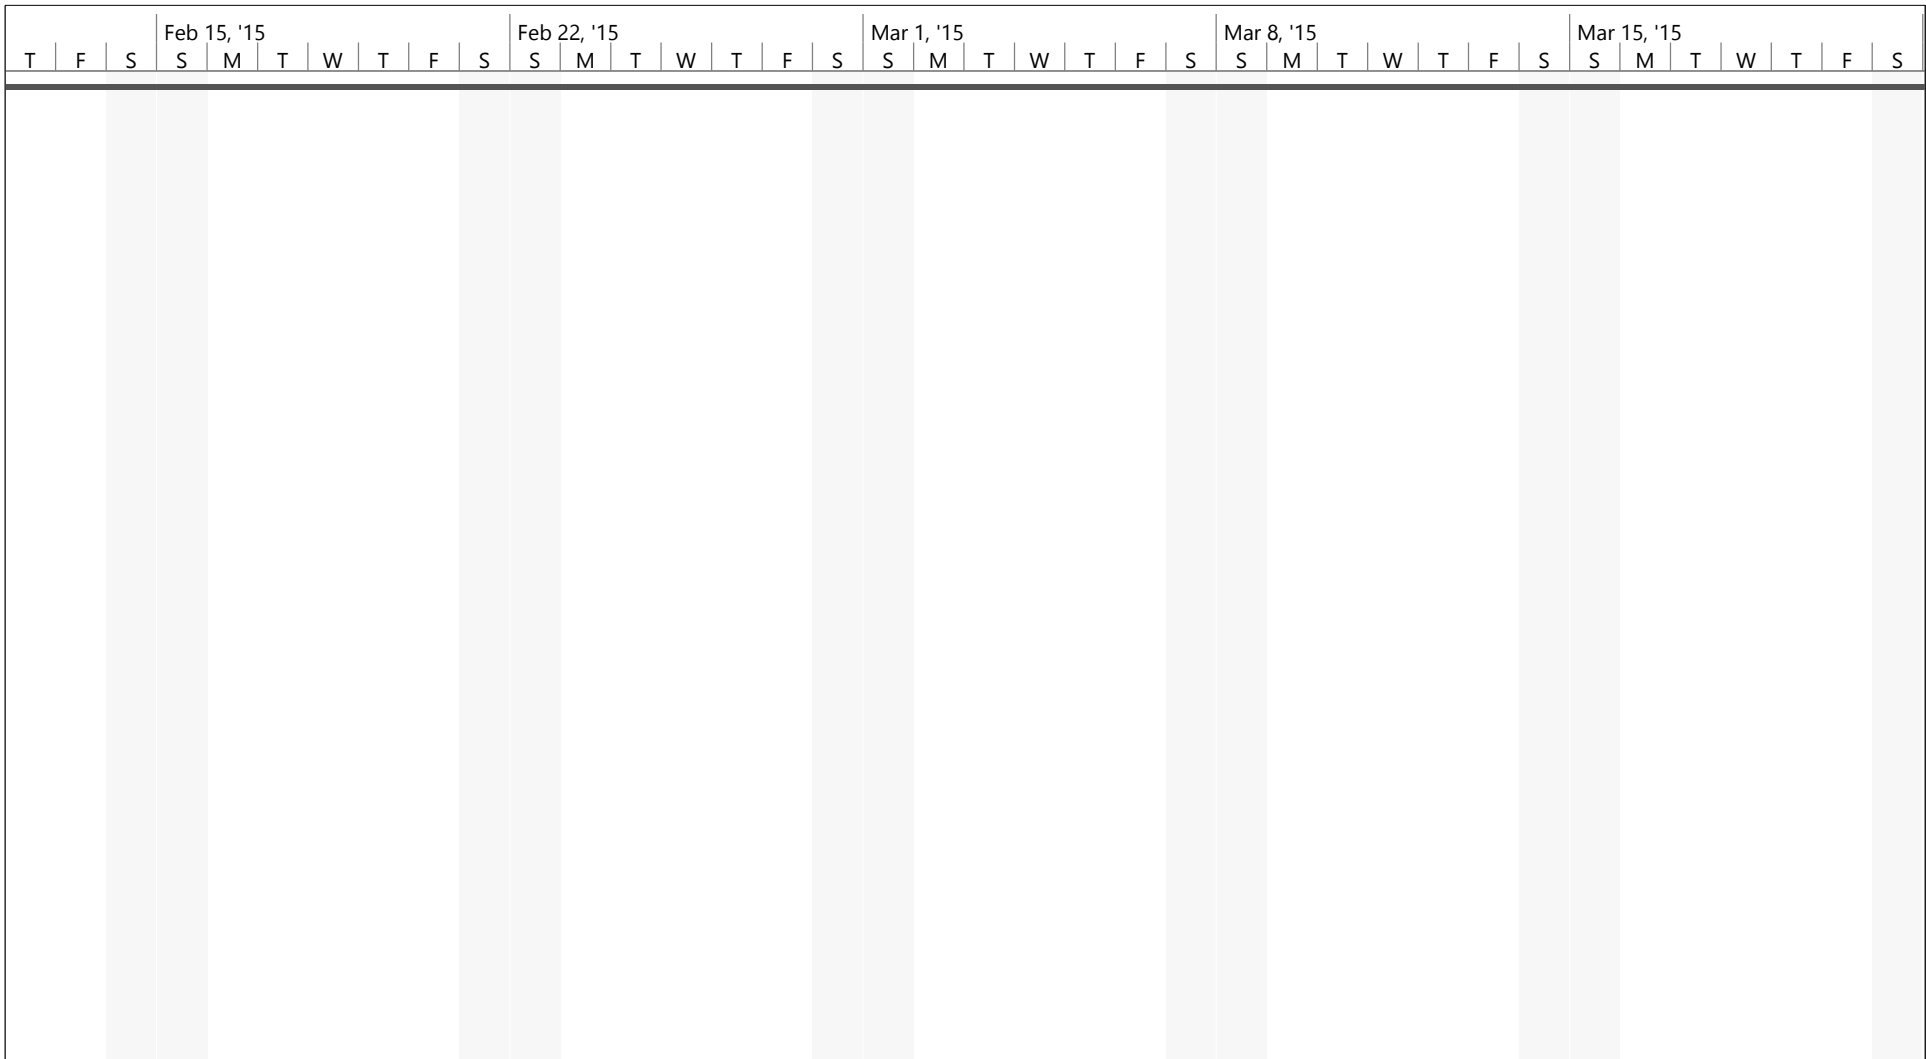



Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

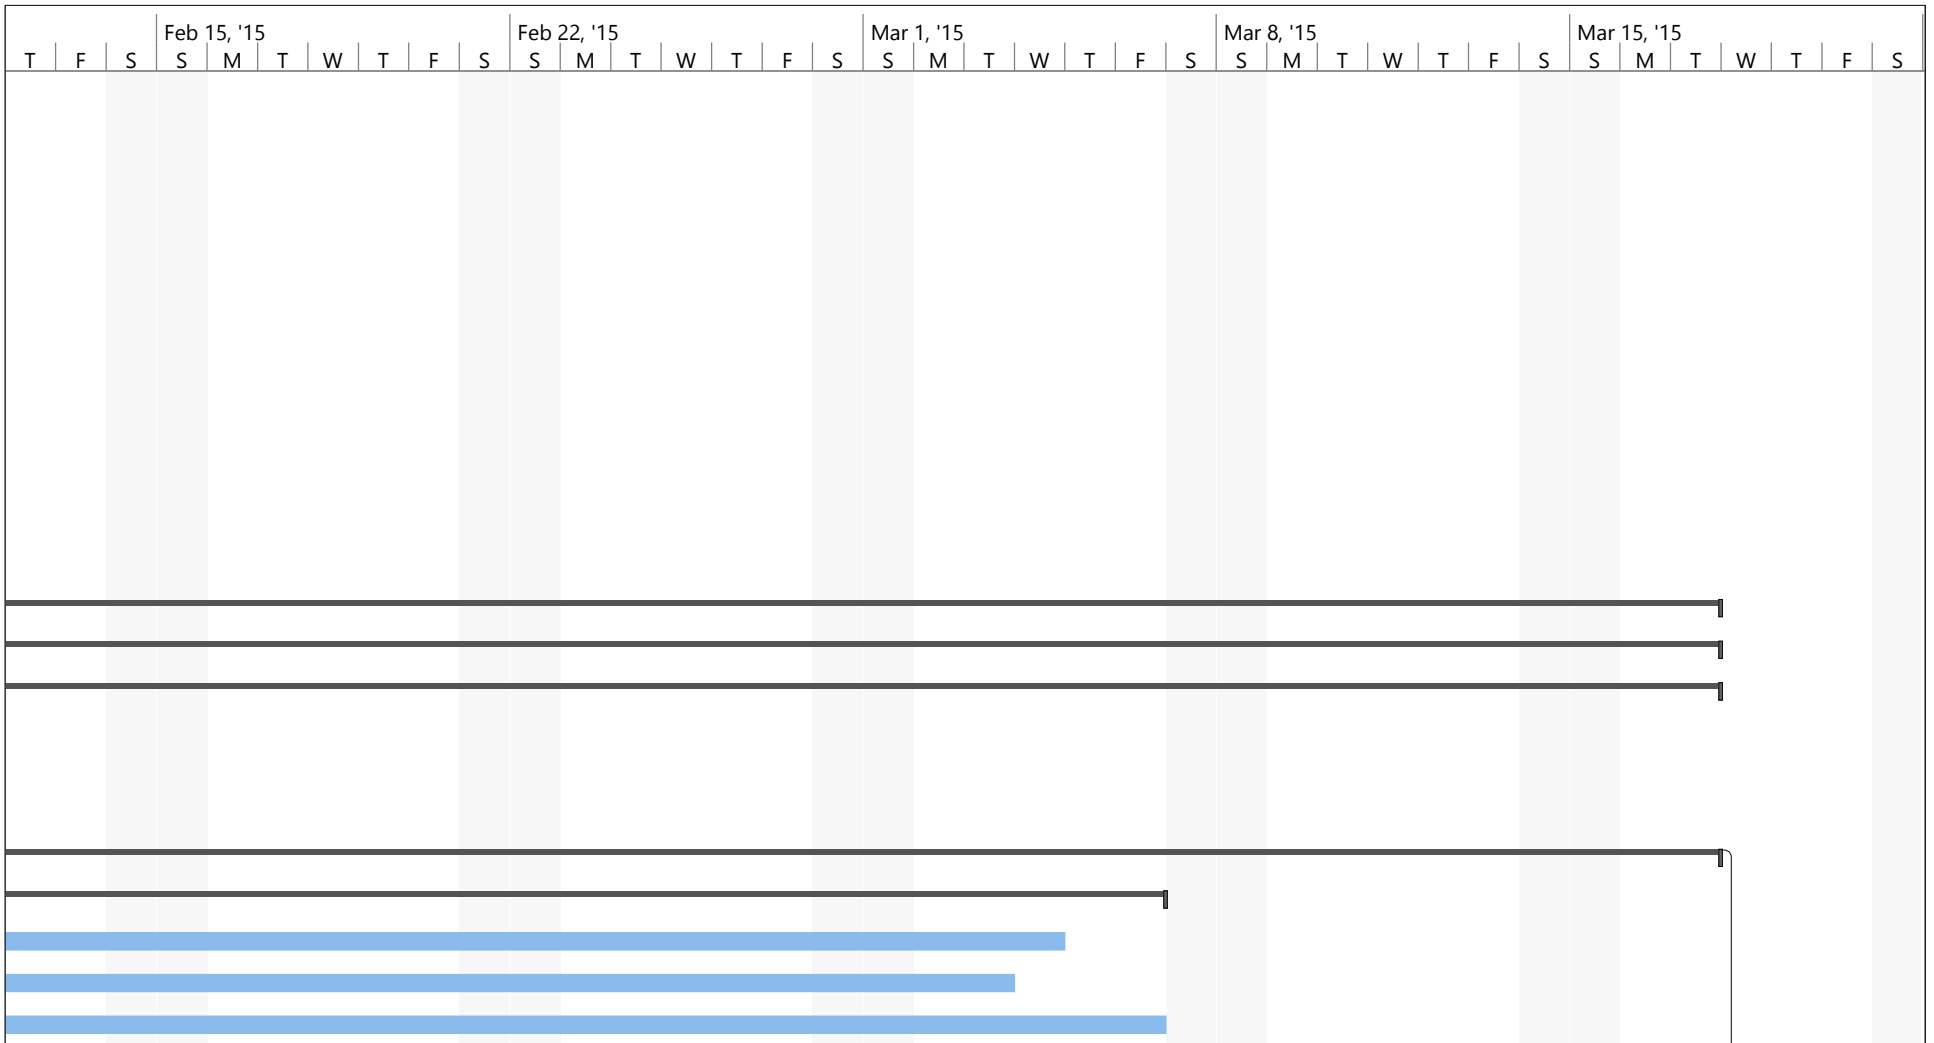


Project: Third-Eye Developmen Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

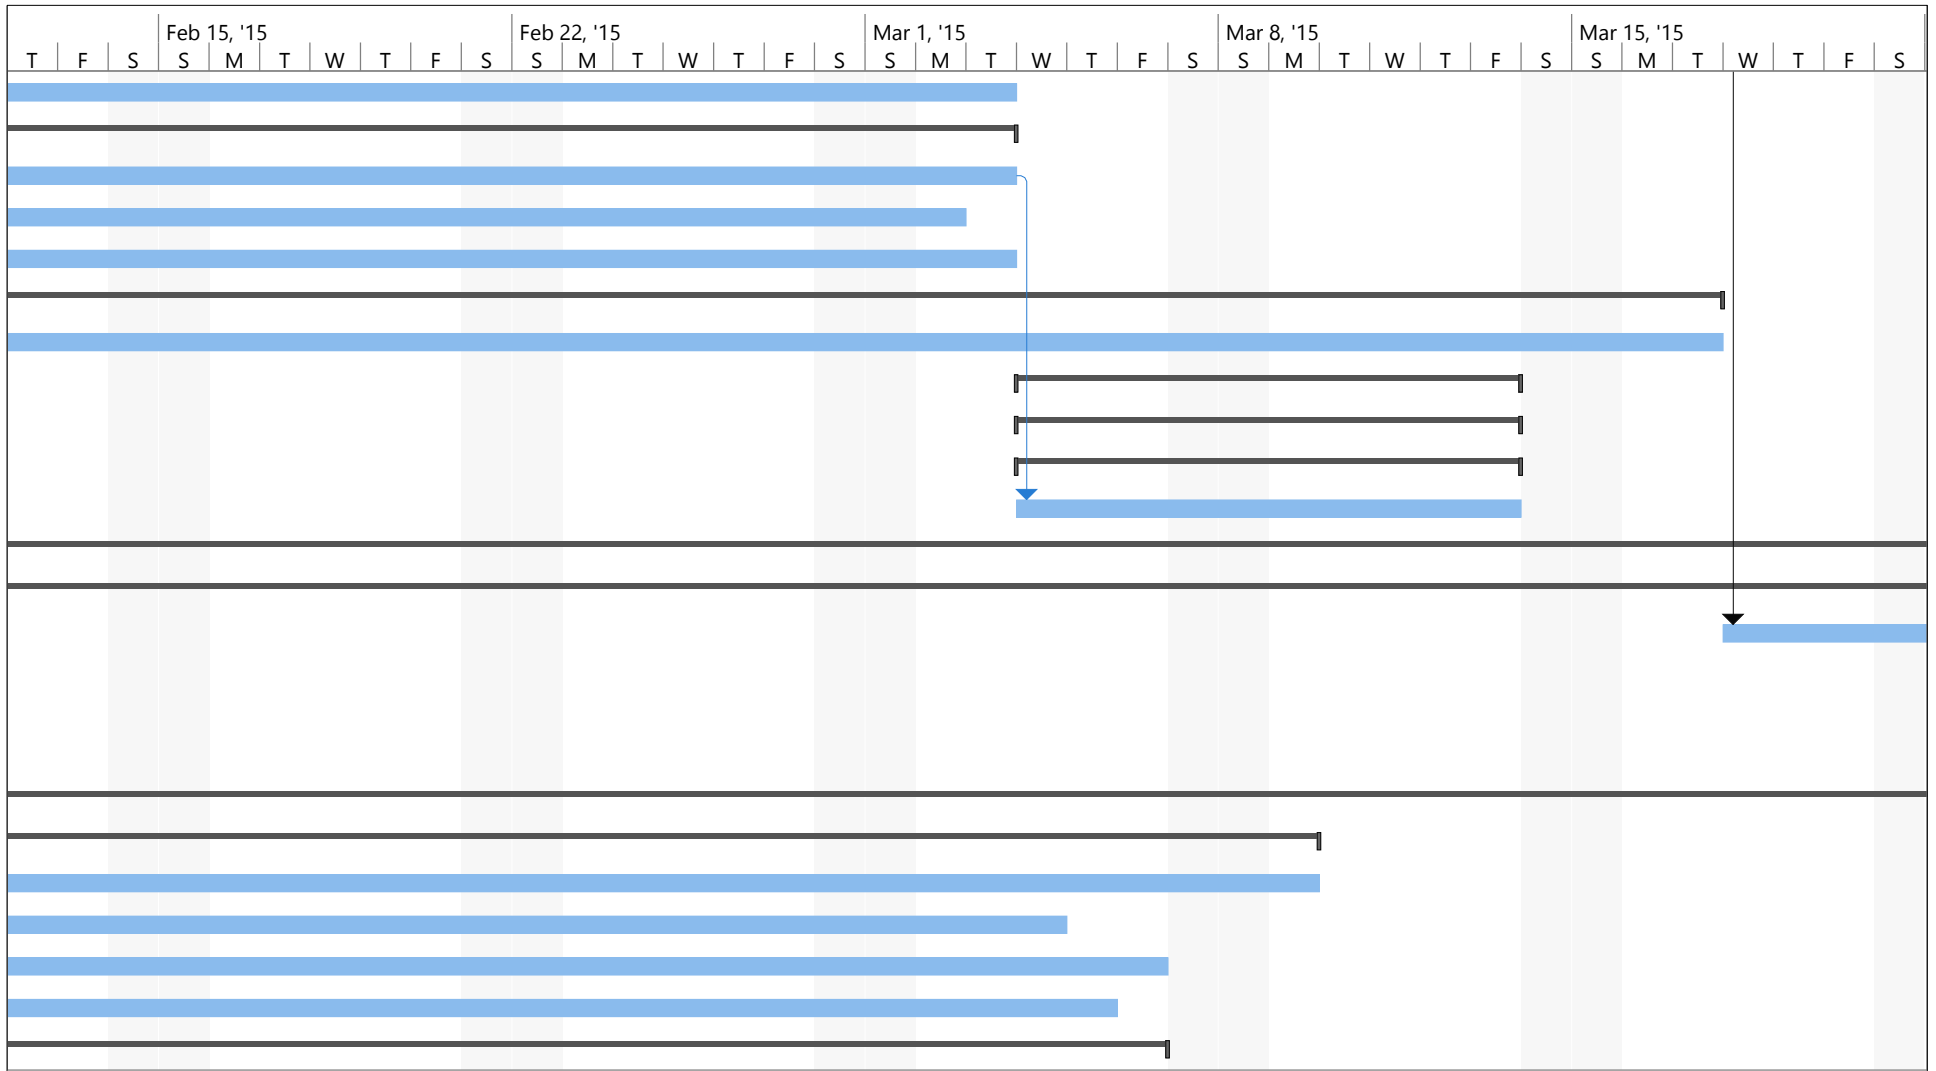

Project: Third-Eye Developmen
Date: Sun 12/7/14

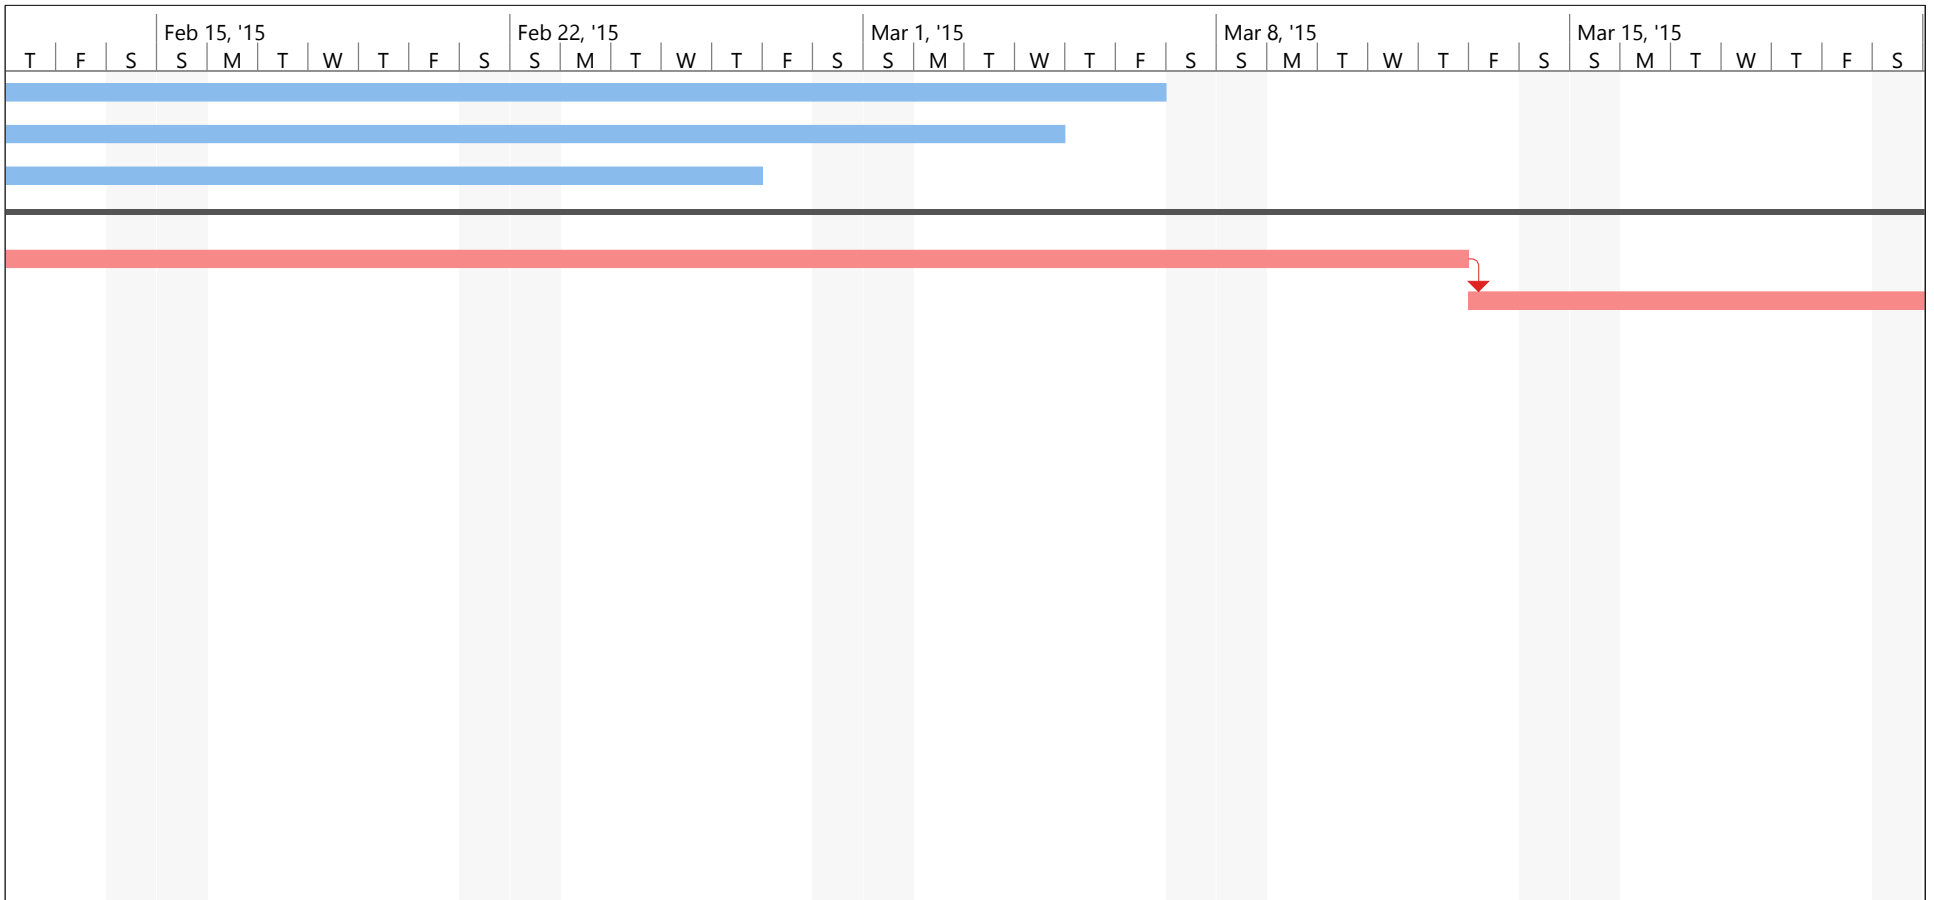


Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

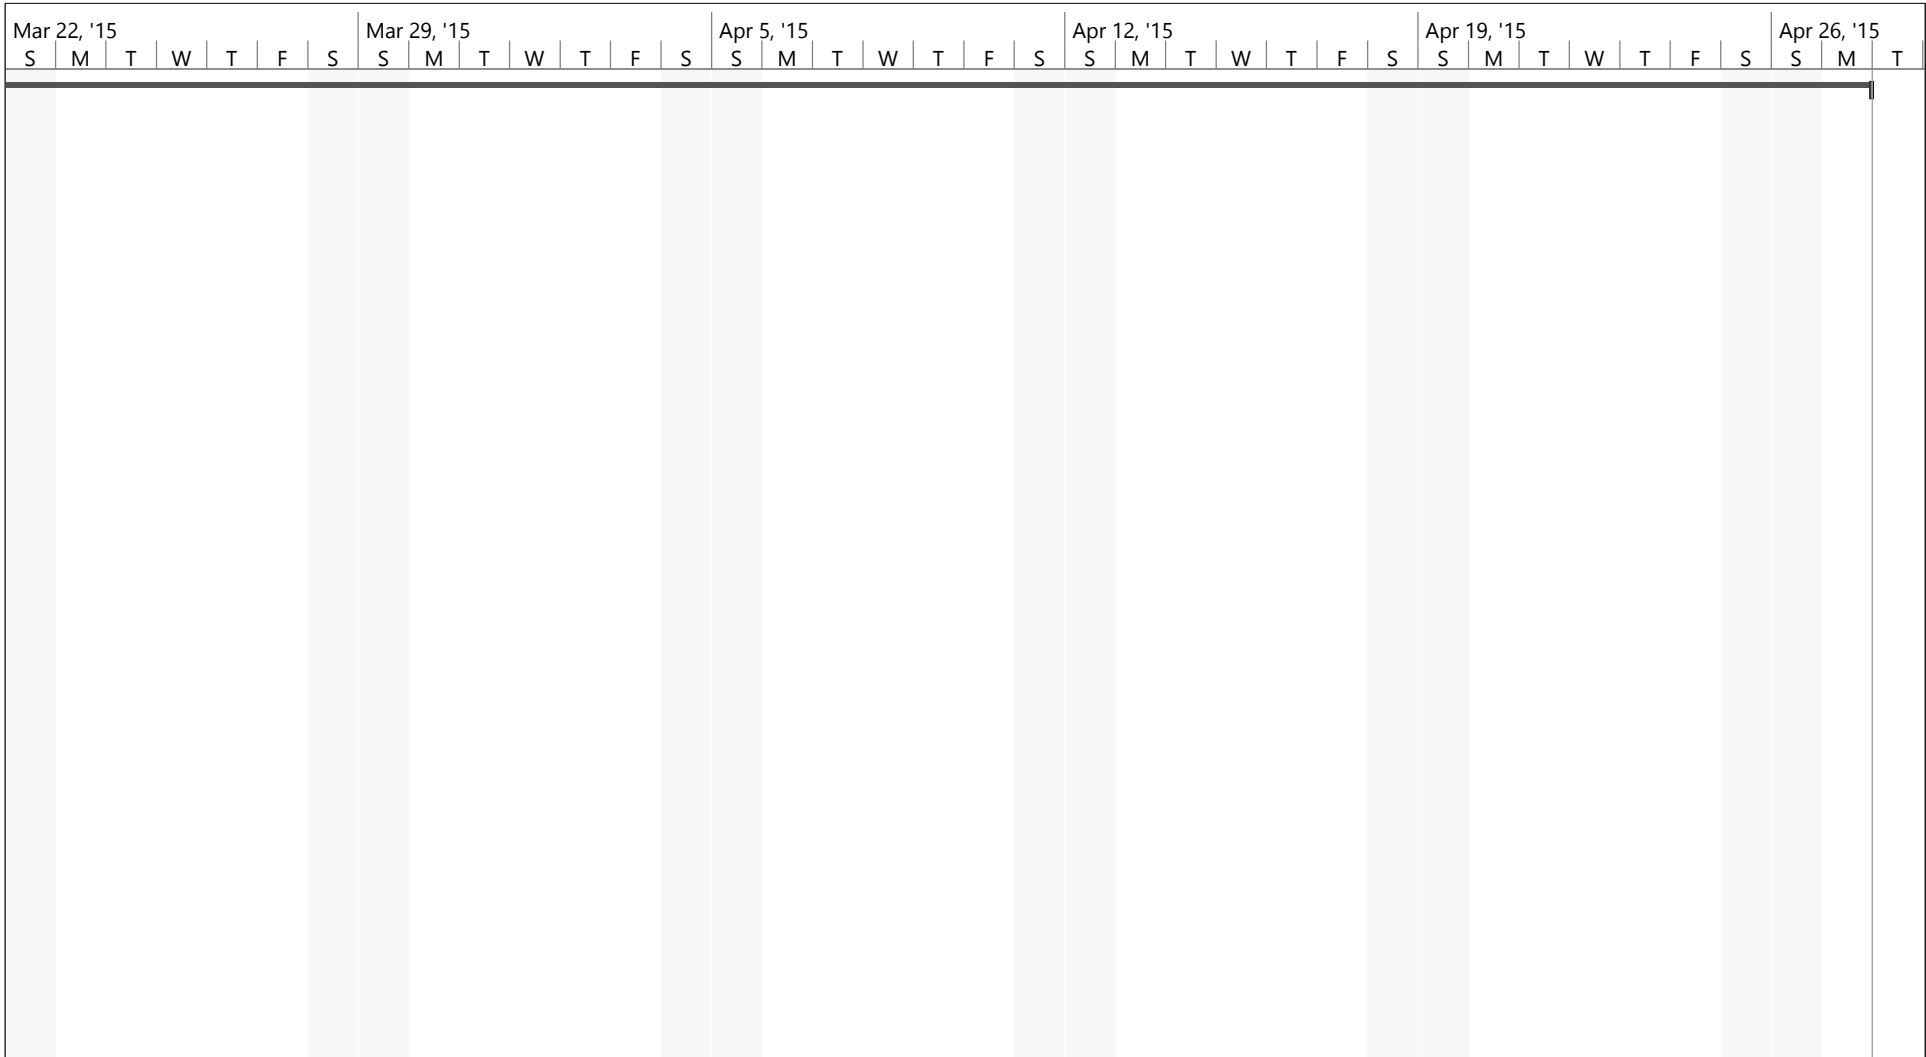

Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	





Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

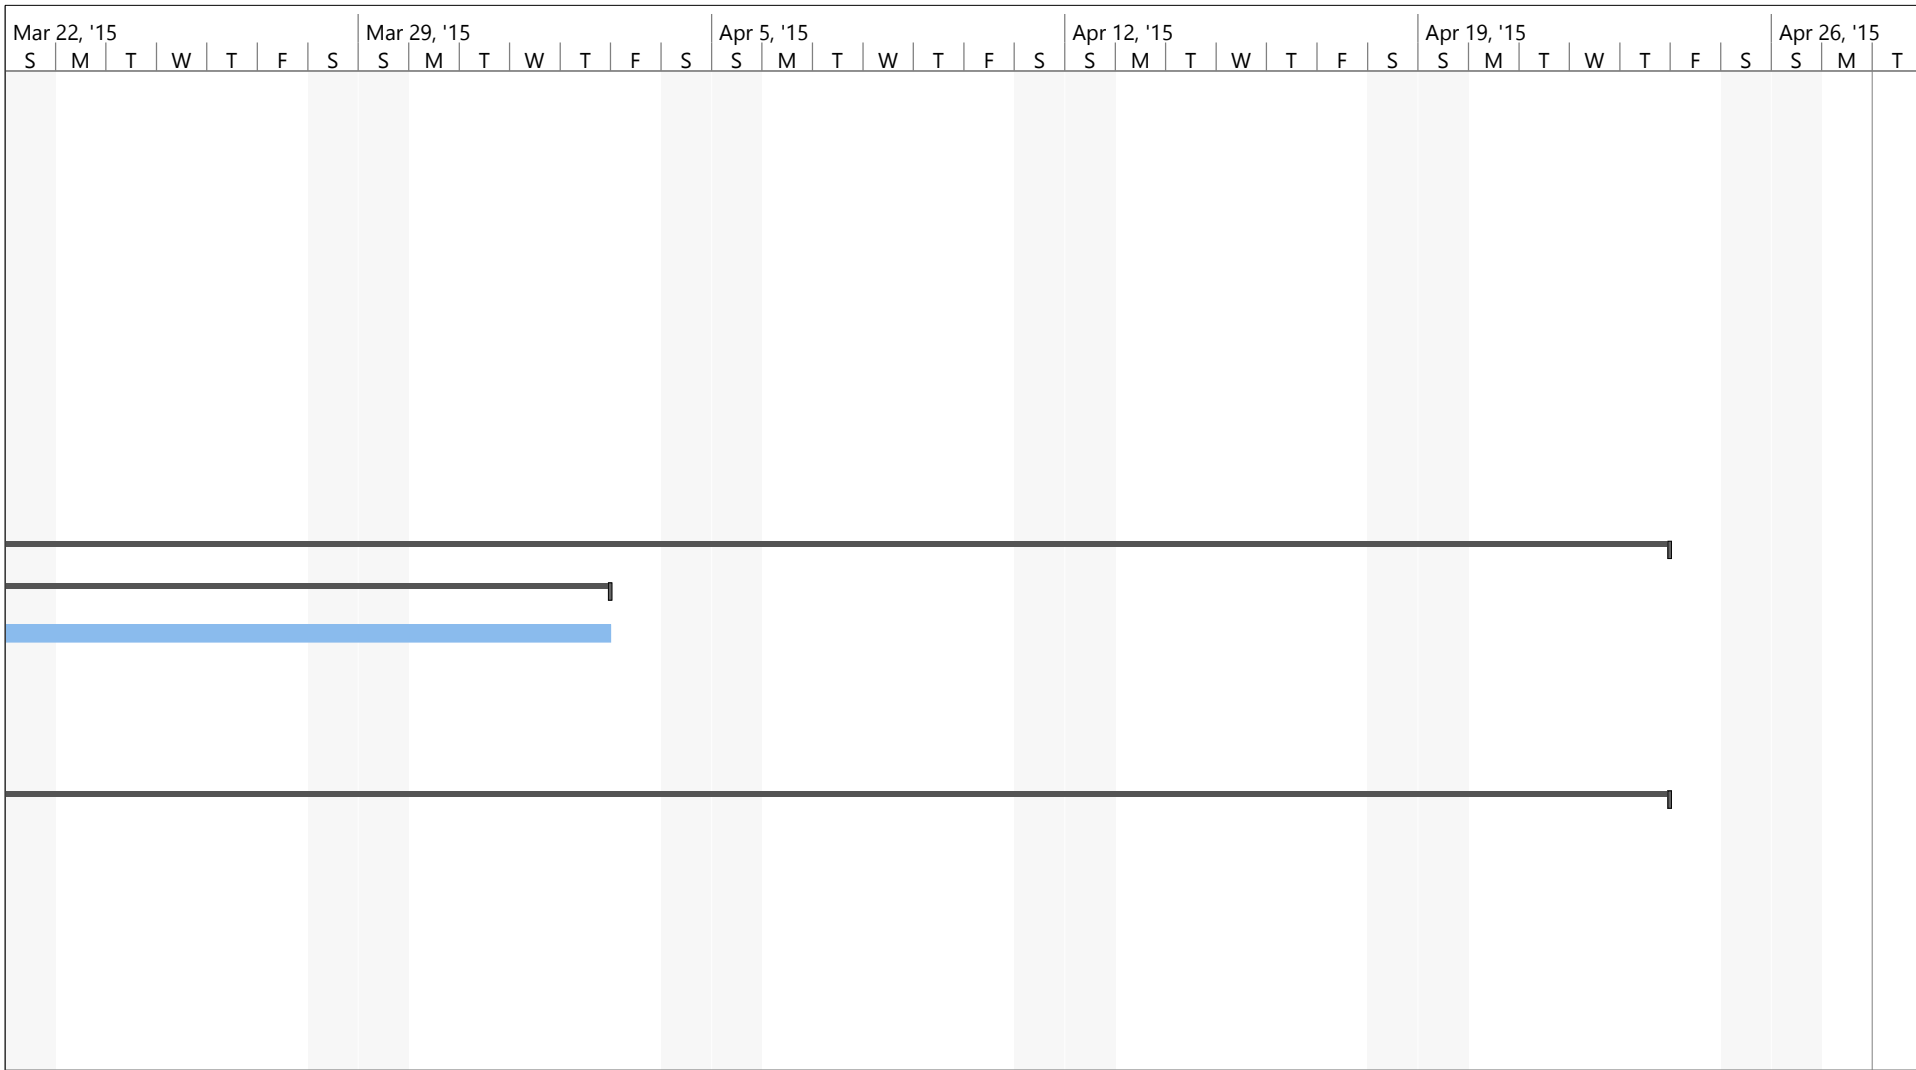

Project: Third-Eye Development
Date: Sun 12/7/14

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	

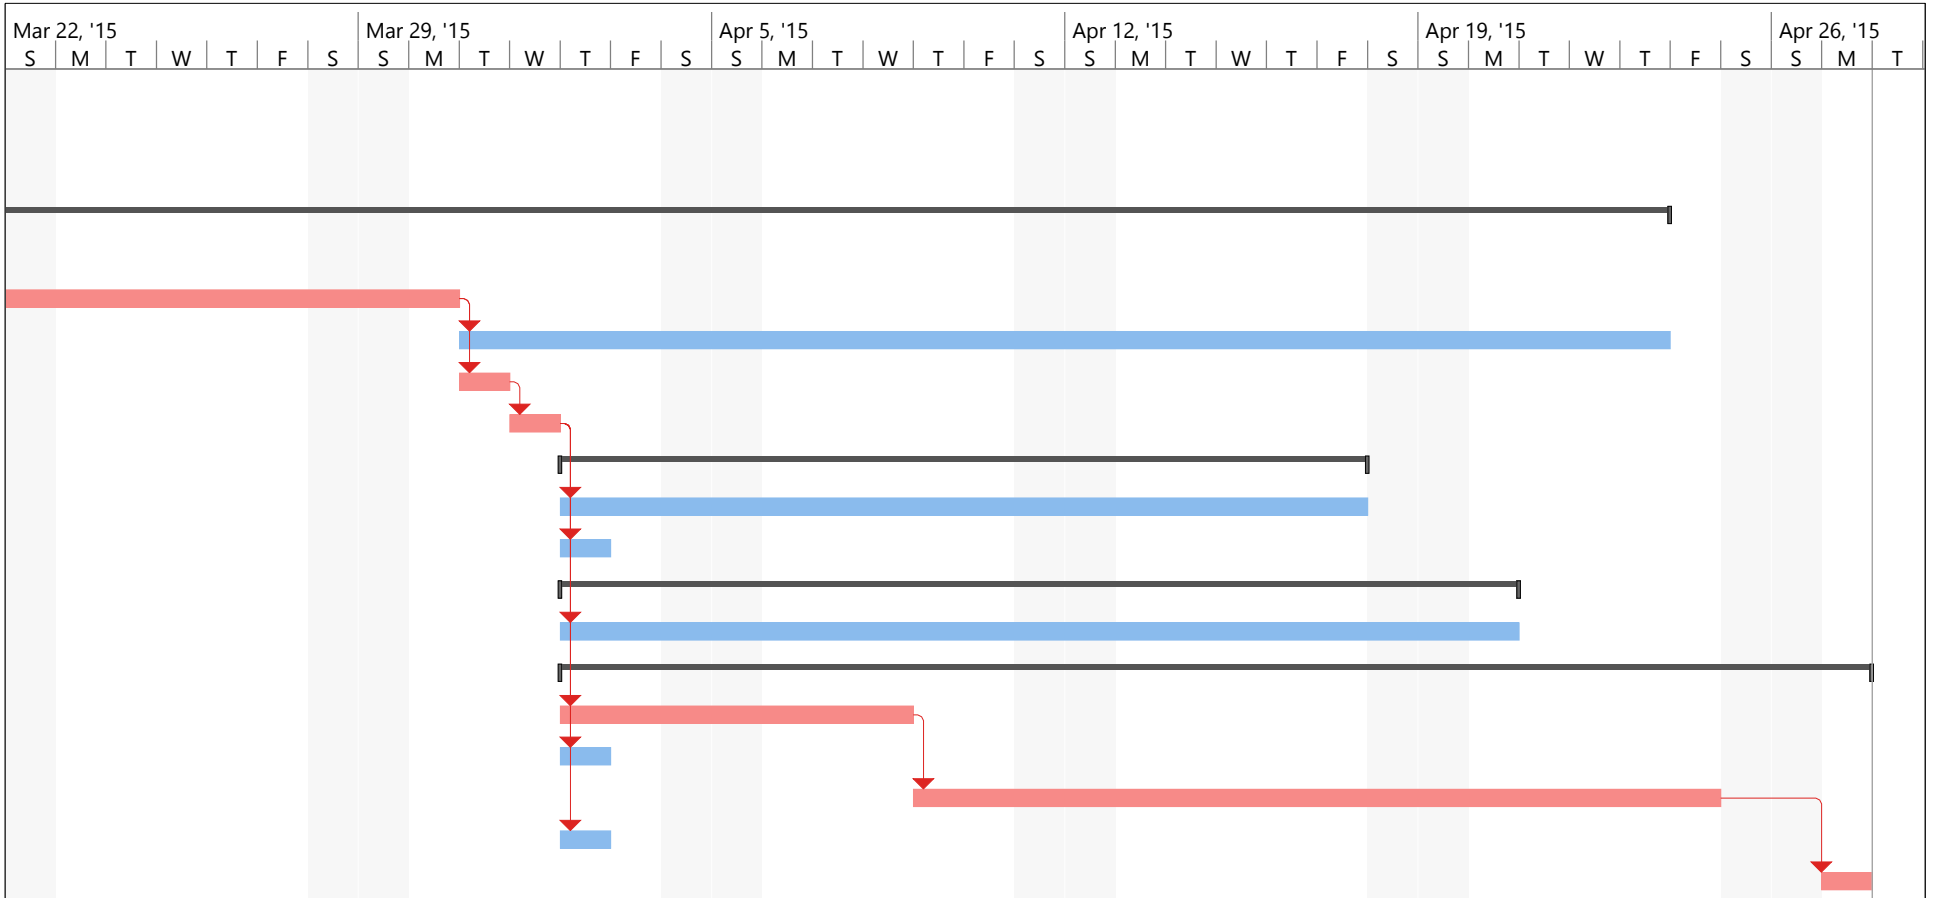

Project: Third-Eye Development Date: Sun 12/7/14	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	
